


ID	Task Mode	Task Calendar	Task Name	Duration	% Complete	Start	Finish	Actual Start	Actual Finish	Predecessors
1		Standard	Las Virgenes PV Project	422 days	15%	Tue 1/22/19	Sun 9/13/20	Tue 1/22/19		NA
2		Standard	Project Award	1 day	100%	Tue 1/22/19	Tue 1/22/19	Tue 1/22/19	Tue 1/22/19	
3		Standard	Internal Kickoff Meeting	1 day	100%	Fri 2/1/19	Fri 2/1/19	Fri 2/1/19	Fri 2/1/19	2
4		Standard	EPC Closing	182 days	21%	Mon 3/11/19	Mon 11/25/19	Mon 3/11/19		NA
5		Standard	Real Estate/Title	86 days	56%	Fri 5/31/19	Tue 10/1/19	Fri 5/31/19		NA
6		Standard	License Agreement Agreed Upon	25 days	100%	Fri 5/31/19	Fri 7/5/19	Fri 5/31/19	Fri 7/5/19	17,37FF,40
7		Standard	License Agreement Executed & Recorded - DELAY (Board Approval)	10 days	0%	Wed 9/4/19	Tue 9/17/19		NA	6,10
8		Standard	Title Policy Issued	10 days	0%	Wed 9/18/19	Tue 10/1/19		NA	7
9		Standard	April Board Meeting	1 day	100%	Thu 3/28/19	Thu 3/28/19	Thu 3/28/19	Thu 3/28/19	2
10		Standard	September Board Meeting	1 day	0%	Tue 9/3/19	Tue 9/3/19		NA	2
11		Standard	Environmental	0 days	100%	Mon 3/11/19	Mon 3/11/19	Mon 3/11/19	Mon 3/11/19	
13		Standard	Conditional Use Permit	4 days	100%	Thu 3/28/19	Tue 4/2/19	Thu 3/28/19	Tue 4/2/19	
16		Standard	Power Purchase Agreement	170 days	87%	Thu 3/28/19	Mon 11/25/19	Thu 3/28/19		NA
17		Standard	PPA Approved by Board	1 day	100%	Thu 3/28/19	Thu 3/28/19	Thu 3/28/19	Thu 3/28/19	9
18		Standard	PPA Fully Executed	3 days	100%	Thu 4/25/19	Tue 4/30/19	Thu 4/25/19	Tue 4/30/19	17FS+10 days
19		Standard	PPA Amendment Negotiations	23 days	96%	Fri 7/19/19	Wed 8/21/19	Fri 7/19/19		NA 51,18
20		Standard	PPA Amendment Approved by Board	0 days	0%	Tue 9/3/19	Tue 9/3/19		NA	10,19
21		Standard	PPA Amendment Fully Executed	3 days	0%	Wed 9/4/19	Fri 9/6/19		NA	20
22		Standard	NTP (From JPA)	0 days	0%	Mon 11/25/19	Mon 11/25/19		NA	33
23		Standard	EPC Contract	43 days	0%	Tue 9/3/19	Sat 11/2/19		NA	NA
24		Standard	Close Financing, MIPA & EPC Executed	60 edays	0%	Tue 9/3/19	Sat 11/2/19		NA	NA 8FF,15,12,36,40,
25		Standard	NTP (From Buyer)	0 days	0%	Sat 11/2/19	Sat 11/2/19		NA	NA 24,21
26		None	PPA Conditions Precedent	191 days	14%	Wed 2/27/19	Mon 11/25/19	Wed 2/27/19		NA
27		Standard	BSS Submits COIs	1 day	100%	Wed 2/27/19	Wed 2/27/19	Wed 2/27/19	Wed 2/27/19	3
28		Standard	BSS Submits EPC	1 day	0%	Mon 11/4/19	Mon 11/4/19		NA	NA 24
29		Standard	BSS Provides Written Assessment of Utility Facilities' Capacity	1 day	0%	Fri 9/27/19	Fri 9/27/19		NA	NA 54
30		Standard	BSS Submits 90% Design for JPA Approval	1 day	0%	Fri 9/27/19	Fri 9/27/19		NA	NA 54
31		Standard	BSS Provides Proof of Financing	1 day	0%	Mon 11/4/19	Mon 11/4/19		NA	NA 24
32		Standard	BSS Obtains All Permits for Construction	1 day	0%	Fri 11/22/19	Fri 11/22/19		NA	NA 79
33		Standard	Completion of Conditions Precedent	1 day	0%	Mon 11/25/19	Mon 11/25/19		NA	NA 27,28,29,30,31,3
34		Standard	Site Discovery	79 days	100%	Thu 2/7/19	Thu 5/30/19	Thu 2/7/19	Thu 5/30/19	
43		Standard	Engineering	180 days	69%	Tue 3/12/19	Fri 11/22/19	Tue 3/12/19		NA
44		Standard	ODF Kickoff/System Design Start	0 days	100%	Tue 3/12/19	Tue 3/12/19	Tue 3/12/19	Tue 3/12/19	37
45		Standard	50% Design	8 days	100%	Wed 3/13/19	Fri 3/22/19	Wed 3/13/19	Fri 3/22/19	44
46		Standard	50% Design Release	0 days	100%	Tue 3/26/19	Tue 3/26/19	Tue 3/26/19	Tue 3/26/19	45
47		Standard	Host Review of 50%	8 days	100%	Wed 3/27/19	Fri 4/5/19	Wed 3/27/19	Fri 4/5/19	46
48		Standard	DELAY - Fire Dept Preliminary Approval (Access Roads)	40 days	100%	Wed 3/27/19	Tue 5/21/19	Wed 3/27/19	Tue 5/21/19	46
49		Standard	CD IFR Design	38 days	100%	Mon 4/8/19	Thu 5/30/19	Mon 4/8/19	Thu 5/30/19	46,47,41FF
50		Standard	DELAY - Confirm Additional Drainage Scope	32 days	100%	Mon 4/15/19	Wed 5/29/19	Mon 4/15/19	Wed 5/29/19	41
51		Standard	DELAY - Agreement on Rough Road Markup	9 days	100%	Mon 7/1/19	Fri 7/12/19	Mon 7/1/19	Fri 7/12/19	49,48,50
52		Standard	DELAY - FD Approval of Rough Road Markup	20 days	100%	Mon 7/15/19	Fri 8/9/19	Mon 7/15/19	Fri 8/9/19	51
53		Standard	CD IFR Design - Continued	30 days	13%	Thu 8/15/19	Thu 9/26/19	Thu 8/15/19		NA 52
54		Standard	CD IFR Release	0 days	0%	Thu 9/26/19	Thu 9/26/19		NA	NA 42,53,80
55		Standard	Host Review of IFR	10 days	0%	Fri 9/27/19	Thu 10/10/19		NA	NA 54,40
56		Standard	Owner Review of IFR	10 days	0%	Fri 9/27/19	Thu 10/10/19		NA	NA 54
57		Standard	CD IFP Design	5 days	0%	Fri 10/11/19	Thu 10/17/19		NA	NA 55,56
58		Standard	CD IFP Release	0 days	0%	Thu 10/17/19	Thu 10/17/19		NA	NA 57
59		Standard	Host Review of IFP	10 days	0%	Fri 10/18/19	Thu 10/31/19		NA	NA 58
60		Standard	Owner Review of IFP	10 days	0%	Fri 10/18/19	Thu 10/31/19		NA	NA 58
61		Standard	CD IFC Design	1 day	0%	Fri 11/22/19	Fri 11/22/19		NA	NA 79
62		Standard	CD IFC Release	0 days	0%	Fri 11/22/19	Fri 11/22/19		NA	NA 61
63		Standard	Interconnection	359 days	9%	Wed 1/23/19	Wed 6/17/20	Wed 1/23/19		NA
64		Standard	GIA Executed	0 days	100%	Wed 1/23/19	Wed 1/23/19	Wed 1/23/19	Wed 1/23/19	2

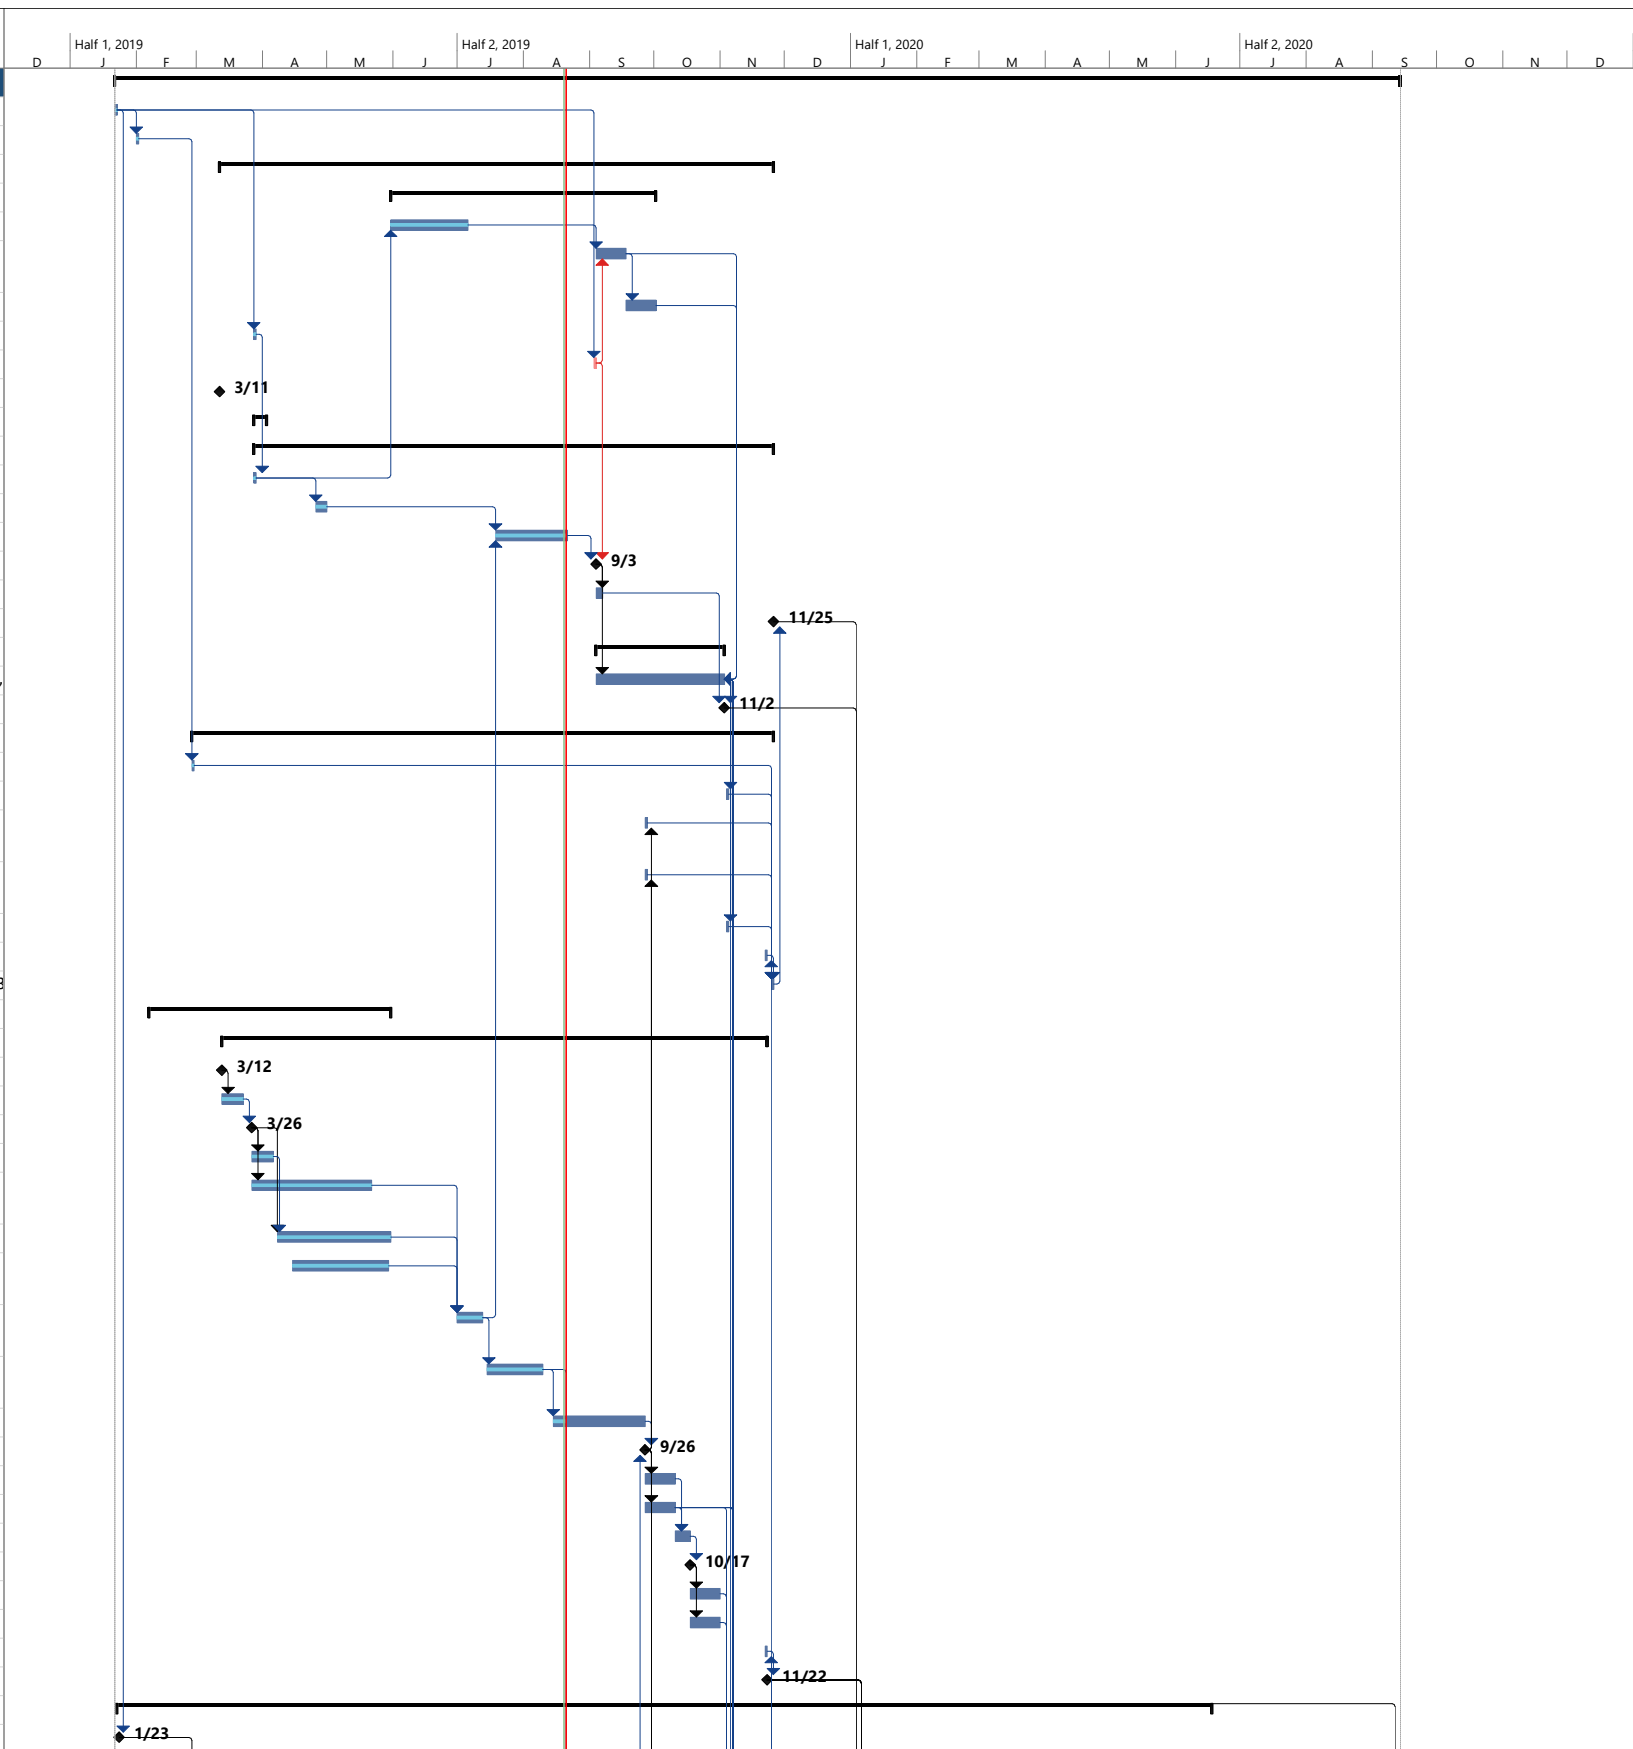

Project: Las Virgenes CPM 03.26
Date: Tue 8/20/19

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress

ID	Task Mode	Task Calendar	Task Name	Duration	% Complete	Start	Finish	Actual Start	Actual Finish	Predecessors	Gantt Chart (Half 1, 2019; Half 2, 2019; Half 1, 2020; Half 2, 2020)																											
65	Standard	Standard	Intx Fees Paid & Engineer Assigned	15 days	100%	Wed 2/27/19	Tue 3/19/19	Wed 2/27/19	Tue 3/19/19	64	[Gantt bar for task 65]																											
66	Standard	Standard	BSS Prepares/Submits SCE Design Package	35 days	0%	Fri 9/27/19	Thu 11/14/19	NA	NA	65,54	[Gantt bar for task 66]																											
67	Standard	Standard	BSS Submits SWGR Drawings	1 day	0%	Mon 12/9/19	Mon 12/9/19	NA	NA	84FS+20 days	[Gantt bar for task 67]																											
68	Standard	Standard	SCE Approves Design Package	1 day	0%	Fri 11/15/19	Fri 11/15/19	NA	NA	66	[Gantt bar for task 68]																											
69	Standard	Standard	SCE Approves SWGR Drawings	20 days	0%	Tue 12/10/19	Wed 1/8/20	NA	NA	67	[Gantt bar for task 69]																											
70	Standard	Standard	SCE Design & Estimating	60 days	0%	Thu 1/9/20	Wed 4/1/20	NA	NA	68,69	[Gantt bar for task 70]																											
71	Standard	Standard	SCE Issues Design & Estimate	5 days	0%	Thu 4/2/20	Wed 4/8/20	NA	NA	70	[Gantt bar for task 71]																											
72	Standard	Standard	SCE Construction Lead Time	23 days	0%	Thu 4/30/20	Mon 6/1/20	NA	NA	139	[Gantt bar for task 72]																											
73	Standard	Standard	SCE Construction	1 day	0%	Tue 6/2/20	Tue 6/2/20	NA	NA	72	[Gantt bar for task 73]																											
74	Standard	Standard	Request PTO	0 days	0%	Tue 6/2/20	Tue 6/2/20	NA	NA	72,163,73	[Gantt bar for task 74]																											
75	Standard	Standard	Witness Testing/PTO Inspection	10 days	0%	Wed 6/3/20	Tue 6/16/20	NA	NA	74	[Gantt bar for task 75]																											
76	Standard	Standard	Conditional PTO Issued	0 days	0%	Tue 6/16/20	Tue 6/16/20	NA	NA	75	[Gantt bar for task 76]																											
77	Standard	Standard	Commercial Operation Date	1 day	0%	Wed 6/17/20	Wed 6/17/20	NA	NA	76	[Gantt bar for task 77]																											
78	Standard	Standard	Permitting	66 days	0%	Wed 8/21/19	Thu 11/21/19	NA	NA	NA	[Gantt bar for task 78]																											
79	Standard	Standard	AHJ Review	15 days	0%	Fri 11/1/19	Thu 11/21/19	NA	NA	59,60	[Gantt bar for task 79]																											
80	Standard	Standard	FD Formal Approval	5 days	0%	Wed 8/21/19	Tue 8/27/19	NA	NA	52	[Gantt bar for task 80]																											
81	Standard	Standard	Procurement	130 days	0%	Fri 9/27/19	Tue 3/31/20	NA	NA	NA	[Gantt bar for task 81]																											
82	Standard	Standard	Subcontractor Buyout	40 days	0%	Fri 9/27/19	Thu 11/21/19	NA	NA	54	[Gantt bar for task 82]																											
83	None	Standard	SWBD	101 days	0%	Thu 11/7/19	Tue 3/31/20	NA	NA	NA	[Gantt bar for task 83]																											
84	Standard	Standard	Release Switchboard PO	1 day	0%	Thu 11/7/19	Thu 11/7/19	NA	NA	24FS+3 days,56	[Gantt bar for task 84]																											
85	Standard	Standard	SWBD Lead Time	20 wks	0%	Fri 11/8/19	Tue 3/31/20	NA	NA	84	[Gantt bar for task 85]																											
86	None	Standard	PNL-1	41 days	0%	Mon 11/4/19	Thu 1/2/20	NA	NA	NA	[Gantt bar for task 86]																											
87	Standard	Standard	Release PNL-1 PO	1 day	0%	Mon 11/4/19	Mon 11/4/19	NA	NA	24,56	[Gantt bar for task 87]																											
88	Standard	Standard	PNL-1 Lead Time	40 days	0%	Tue 11/5/19	Thu 1/2/20	NA	NA	87	[Gantt bar for task 88]																											
89	None	Standard	MV XFMR	101 days	0%	Thu 11/7/19	Tue 3/31/20	NA	NA	NA	[Gantt bar for task 89]																											
90	Standard	Standard	Release MV XFMR PO	1 day	0%	Thu 11/7/19	Thu 11/7/19	NA	NA	24FS+3 days,56	[Gantt bar for task 90]																											
91	Standard	Standard	MV XFMR Lead Time	100 days	0%	Fri 11/8/19	Tue 3/31/20	NA	NA	90	[Gantt bar for task 91]																											
92	None	Standard	Modules	84 days	0%	Thu 11/7/19	Fri 3/6/20	NA	NA	NA	[Gantt bar for task 92]																											
93	Standard	Standard	Release Module PO	1 day	0%	Thu 11/7/19	Thu 11/7/19	NA	NA	24FS+3 days,56	[Gantt bar for task 93]																											
94	Standard	Standard	Module Lead Time	120 edays	0%	Thu 11/7/19	Fri 3/6/20	NA	NA	93	[Gantt bar for task 94]																											
95	None	Standard	Foundations	61 days	0%	Tue 10/29/19	Fri 1/24/20	NA	NA	NA	[Gantt bar for task 95]																											
96	Standard	Standard	Release Foundations PO	1 day	0%	Tue 10/29/19	Tue 10/29/19	NA	NA	99FF-7 days	[Gantt bar for task 96]																											
97	Standard	Standard	Foundation Lead Time	30 days	0%	Thu 12/12/19	Fri 1/24/20	NA	NA	96,100FF-7 days	[Gantt bar for task 97]																											
98	None	Standard	Tracker	61 days	0%	Thu 11/7/19	Tue 2/4/20	NA	NA	NA	[Gantt bar for task 98]																											
99	Standard	Standard	Release Tracker PO	1 day	0%	Thu 11/7/19	Thu 11/7/19	NA	NA	24FS+3 days,56	[Gantt bar for task 99]																											
100	Standard	Standard	Tracker Lead Time	60 days	0%	Fri 11/8/19	Tue 2/4/20	NA	NA	99	[Gantt bar for task 100]																											
101	None	Standard	Inverter	91 days	0%	Thu 11/7/19	Tue 3/17/20	NA	NA	NA	[Gantt bar for task 101]																											
102	Standard	Standard	Release Inverter PO	1 day	0%	Thu 11/7/19	Thu 11/7/19	NA	NA	24FS+3 days,56	[Gantt bar for task 102]																											
103	Standard	Standard	Inverter Lead Time	90 days	0%	Fri 11/8/19	Tue 3/17/20	NA	NA	102	[Gantt bar for task 103]																											
104	None	Standard	DAS	31 days	0%	Thu 11/7/19	Fri 12/20/19	NA	NA	NA	[Gantt bar for task 104]																											
105	Standard	Standard	Release DAS PO	1 day	0%	Thu 11/7/19	Thu 11/7/19	NA	NA	24FS+3 days,56	[Gantt bar for task 105]																											
106	Standard	Standard	DAS Lead Time	30 days	0%	Fri 11/8/19	Fri 12/20/19	NA	NA	105	[Gantt bar for task 106]																											
107	Standard	Standard	Construction	108 days	0%	Mon 1/6/20	Wed 6/3/20	NA	NA	NA	[Gantt bar for task 107]																											
108	Standard	Standard	Mobilization	5 days	0%	Mon 1/6/20	Fri 1/10/20	NA	NA	NA	[Gantt bar for task 108]																											
109	Standard	Standard	Mobilization	0 days	0%	Mon 1/6/20	Mon 1/6/20	NA	NA	25,22,97FS-15 da	[Gantt bar for task 109]																											
110	Standard	Standard	Temp Services Setup	5 days	0%	Mon 1/6/20	Fri 1/10/20	NA	NA	62FS+10 days,82	[Gantt bar for task 110]																											
111	Standard	Standard	Safety/HR Materials	5 days	0%	Mon 1/6/20	Fri 1/10/20	NA	NA	62FS+10 days,82	[Gantt bar for task 111]																											
112	Standard	Standard	SWPPP BMP's in Place	5 days	0%	Mon 1/6/20	Fri 1/10/20	NA	NA	62FS+10 days,82	[Gantt bar for task 112]																											
113	Standard	Standard	Site Signage in Place	5 days	0%	Mon 1/6/20	Fri 1/10/20	NA	NA	62FS+10 days,82	[Gantt bar for task 113]																											
114	Standard	Standard	Preconstruction Meeting	5 days	0%	Mon 1/6/20	Fri 1/10/20	NA	NA	62FS+10 days,82	[Gantt bar for task 114]																											
115	Standard	Standard	Construction Survey	5 days	0%	Mon 1/6/20	Fri 1/10/20	NA	NA	62FS+10 days,82	[Gantt bar for task 115]																											
116	Standard	Standard	Civil	15 days	0%	Mon 1/13/20	Fri 1/31/20	NA	NA	NA	[Gantt bar for task 116]																											
117	Standard	Standard	Finish Grading & Roads	15 days	0%	Mon 1/13/20	Fri 1/31/20	NA	NA	115,110,111,112	[Gantt bar for task 117]																											
118	Standard	Standard	Mechanical	50 days	0%	Mon 2/3/20	Fri 4/10/20	NA	NA	NA	[Gantt bar for task 118]																											
119	Standard	Standard	Pile Foundation Installation	10 days	0%	Mon 2/3/20	Fri 2/14/20	NA	NA	117,97FS-3 days	[Gantt bar for task 119]																											
120	Standard	Standard	String Inverter Pile Foundation Installation	10 days	0%	Mon 2/17/20	Fri 2/28/20	NA	NA	119	[Gantt bar for task 120]																											
121	Standard	Standard	Racking Installation	15 days	0%	Mon 3/2/20	Fri 3/20/20	NA	NA	120SS+10 days,1	[Gantt bar for task 121]																											

Project: Las Virgenes CPM 03.26
Date: Tue 8/20/19

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress

ID	Task Mode	Task Calendar	Task Name	Duration	% Complete	Start	Finish	Actual Start	Actual Finish	Predecessors	Gantt Chart (Half 1, 2019; Half 2, 2019; Half 1, 2020; Half 2, 2020)											
122	Standard		PV Solar Module Installation	15 days	0%	Mon 3/23/20	Fri 4/10/20	NA	NA	NA 121SS+15 days,9												
123	Standard		Equipment Pad	49 days	0%	Mon 2/3/20	Thu 4/9/20	NA	NA	NA												
124	Standard		Excavate Equipment Pads	5 days	0%	Mon 2/3/20	Fri 2/7/20	NA	NA	NA 119SS												
125	Standard		Install & Stub-Up UG Conduit	5 days	0%	Mon 2/10/20	Fri 2/14/20	NA	NA	NA 106,124												
126	Standard		Backfill & Compaction	3 days	0%	Mon 2/17/20	Wed 2/19/20	NA	NA	NA 125												
127	Standard		Set Forms	3 days	0%	Thu 2/20/20	Mon 2/24/20	NA	NA	NA 126												
128	Standard		Install Rebar	3 days	0%	Tue 2/25/20	Thu 2/27/20	NA	NA	NA 127												
129	Standard		INSPECTION	5 days	0%	Fri 2/28/20	Thu 3/5/20	NA	NA	NA 128												
130	Standard		Place & Finish Concrete	3 days	0%	Fri 3/6/20	Tue 3/10/20	NA	NA	NA 129												
131	Standard		SPECIAL INSPECTION (Concrete)	5 days	0%	Wed 3/11/20	Tue 3/17/20	NA	NA	NA 130												
132	Standard		Concrete Cure	4 edays	0%	Tue 3/10/20	Sat 3/14/20	NA	NA	NA 130												
133	Standard		Set & Anchor SWBD, XFMR	7 days	0%	Wed 4/1/20	Thu 4/9/20	NA	NA	NA 132,131,85,91,8												
134	Standard		Set & Anchor BOS & DAS	2 days	0%	Mon 3/16/20	Tue 3/17/20	NA	NA	NA 132,106												
135	Standard		DC & AC Electrical	56 days	0%	Wed 3/18/20	Wed 6/3/20	NA	NA	NA												
136	Standard		Trench	10 days	0%	Thu 4/9/20	Wed 4/22/20	NA	NA	NA 119SS,71												
137	Standard		Install Underground Conduit	5 days	0%	Thu 4/23/20	Wed 4/29/20	NA	NA	NA 136												
138	Standard		INSPECTION	5 days	0%	Thu 4/30/20	Wed 5/6/20	NA	NA	NA 137												
139	Standard		SCE - UG Civil Release	0 days	0%	Wed 4/29/20	Wed 4/29/20	NA	NA	NA 137												
140	Standard		Backfill & Compaction	5 days	0%	Thu 5/7/20	Wed 5/13/20	NA	NA	NA 138												
141	Standard		Install String Inverters	5 days	0%	Wed 3/18/20	Tue 3/24/20	NA	NA	NA 120,103												
142	Standard		Inter-Module Series Wiring	15 days	0%	Mon 3/30/20	Fri 4/17/20	NA	NA	NA 122FS-10 days												
143	Standard		Install Source Circuits from Strings to Inverters and to Panelboards	15 days	0%	Thu 5/14/20	Wed 6/3/20	NA	NA	NA 122FS-10 days,141,140												
144	Standard		MV Electrical	60 days	0%	Mon 2/17/20	Fri 5/8/20	NA	NA	NA												
145	Standard		Trench	15 days	0%	Mon 2/17/20	Fri 3/6/20	NA	NA	NA 119												
146	Standard		Underground Conduit	10 days	0%	Mon 3/9/20	Fri 3/20/20	NA	NA	NA 145												
147	Standard		INSPECTION	5 days	0%	Mon 3/23/20	Fri 3/27/20	NA	NA	NA 146												
148	Standard		Backfill & Compaction	10 days	0%	Mon 3/30/20	Fri 4/10/20	NA	NA	NA 147												
149	Standard		Install Circuits	10 days	0%	Mon 4/13/20	Fri 4/24/20	NA	NA	NA 148												
150	Standard		MV Terminations	10 days	0%	Mon 4/27/20	Fri 5/8/20	NA	NA	NA 149,133												
151	Standard		DAS Systems	20 days	0%	Wed 3/18/20	Tue 4/14/20	NA	NA	NA												
152	Standard		Install Weather Station	20 days	0%	Wed 3/18/20	Tue 4/14/20	NA	NA	NA 134												
153	Standard		Install Irradiance Meter	20 days	0%	Wed 3/18/20	Tue 4/14/20	NA	NA	NA 134												
154	Standard		Install Tracker Controller(s) & GPS	20 days	0%	Wed 3/18/20	Tue 4/14/20	NA	NA	NA 134												
155	Standard		Install Anemometer	20 days	0%	Wed 3/18/20	Tue 4/14/20	NA	NA	NA 134												
156	Standard		Install DAS BOS (CT's/Data Collector/Modem, etc.)	20 days	0%	Wed 3/18/20	Tue 4/14/20	NA	NA	NA 134												
157	Standard		Installation of Comm Infrastructure	20 days	0%	Wed 3/18/20	Tue 4/14/20	NA	NA	NA 134												
158	Standard		Pre-Operational Commissioning	10 days	0%	Mon 5/11/20	Fri 5/22/20	NA	NA	NA												
159	Standard		DC Source Circuits & Stringing	10 days	0%	Mon 5/11/20	Fri 5/22/20	NA	NA	NA 150												
160	Standard		DC Distribution Feeders	10 days	0%	Mon 5/11/20	Fri 5/22/20	NA	NA	NA 150												
161	Standard		AC Circuits	10 days	0%	Mon 5/11/20	Fri 5/22/20	NA	NA	NA 150												
162	Standard		Transformer Acceptance Testing	10 days	0%	Mon 5/11/20	Fri 5/22/20	NA	NA	NA 150												
163	Standard		AHJ Final	0 days	0%	Fri 5/22/20	Fri 5/22/20	NA	NA	NA 158,152,153,154												
164	Standard		Mechanical Completion	0 days	0%	Wed 6/3/20	Wed 6/3/20	NA	NA	NA 116,118,123,135												
165	Standard		Substantial Completion	0 days	0%	Tue 6/16/20	Tue 6/16/20	NA	NA	NA 76,164,159,160,												
166	Standard		Testing, Commissioning & Acceptance	62 days	0%	Thu 6/18/20	Sun 9/13/20	NA	NA	NA 107,165,75												
167	Standard		Inverters	3 days	0%	Thu 6/18/20	Mon 6/22/20	NA	NA	NA 145,146,147,148												
168	Standard		DAS Configuration	4 days	0%	Tue 6/23/20	Fri 6/26/20	NA	NA	NA 167												
169	Standard		Wash Modules	5 days	0%	Mon 6/29/20	Fri 7/3/20	NA	NA	NA 168												
170	Standard		Final Equipment QA	15 days	0%	Mon 7/6/20	Fri 7/24/20	NA	NA	NA 169												
171	Standard		Performance Testing	15 days	0%	Mon 7/27/20	Fri 8/14/20	NA	NA	NA 170												
172	None		30-Day Continuous Operation	30 edays	0%	Fri 8/14/20	Sun 9/13/20	NA	NA	NA 171												
173	Standard		Closeout	20 days	0%	Mon 8/17/20	Fri 9/11/20	NA	NA	NA												
174	Standard		Punchlist	20 days	0%	Mon 8/17/20	Fri 9/11/20	NA	NA	NA 171												
175	Standard		System Documentation	5 days	0%	Mon 8/17/20	Fri 8/21/20	NA	NA	NA 171												
176	Standard		Final Completion	0 days	0%	Sun 9/13/20	Sun 9/13/20	NA	NA	NA 107,63,173,175,												

Project: Las Virgenes CPM 03.26
Date: Tue 8/20/19

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress
